


Tram route and construction timeline

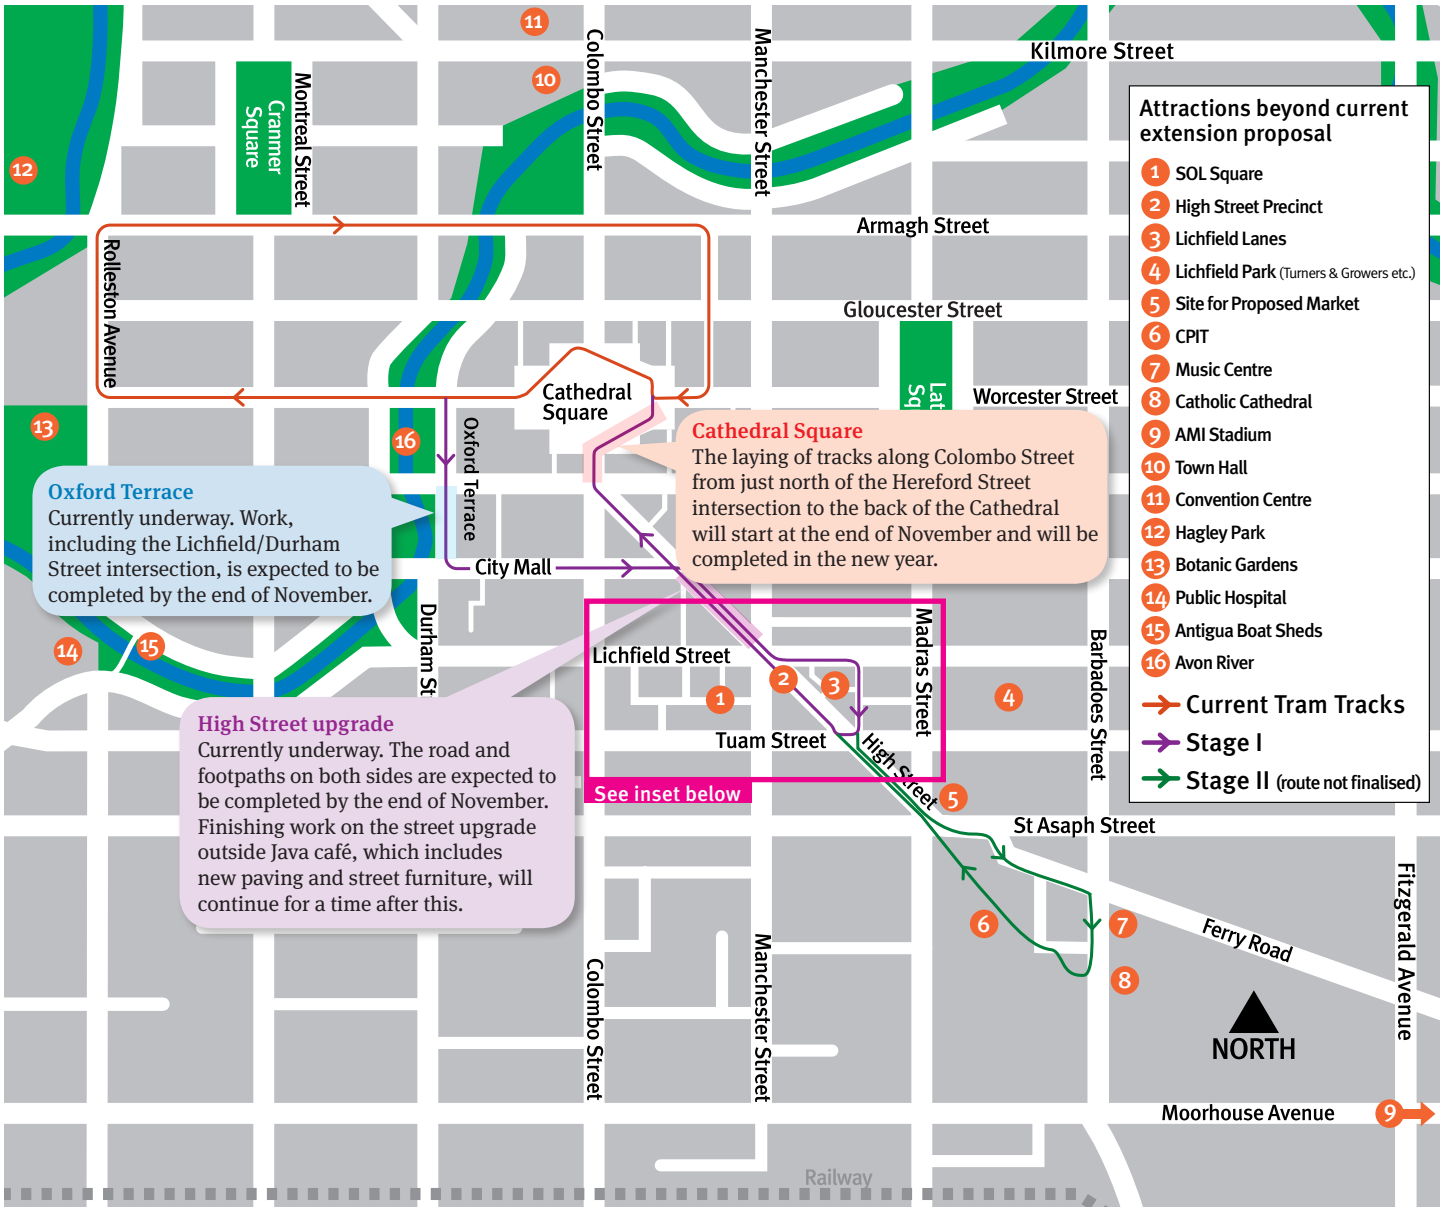

Oxford Terrace
 Currently underway. Work, including the Lichfield/Durham Street intersection, is expected to be completed by the end of November.

High Street upgrade
 Currently underway. The road and footpaths on both sides are expected to be completed by the end of November. Finishing work on the street upgrade outside Java café, which includes new paving and street furniture, will continue for a time after this.

Cathedral Square
 The laying of tracks along Colombo Street from just north of the Hereford Street intersection to the back of the Cathedral will start at the end of November and will be completed in the new year.

Lichfield Street
 See inset below

Manchester St/Lichfield St Intersection
 Work is set to start here on 26 October. It will be carried out in three stages with the aim of keeping one lane of Lichfield Street open at all times.

Lichfield Street
 This short stretch of track will take around six weeks to complete, with work to start in December, following completion of the intersection work.

Poplar Street
 Currently underway. This work will be completed by the end of November.

Tuam Street/High Street
 Work is expected to start in Tuam Street and in the area outside 'Alice in Videoland' in February/March next year. It will then progress through High Street from around March/April 2011.
